

Sprint 1 Review


Campus Marketplace

Date: 13 April 2026

Sprint Duration: 31 March – 13 April (14 days)

Sprint Goal: Deliver a working foundation for the Campus Marketplace, including authentication, role-based routing, item listing creation, editing, type-flagging, and a browsable listings page.

📈 Sprint Progress: Planned vs Actual

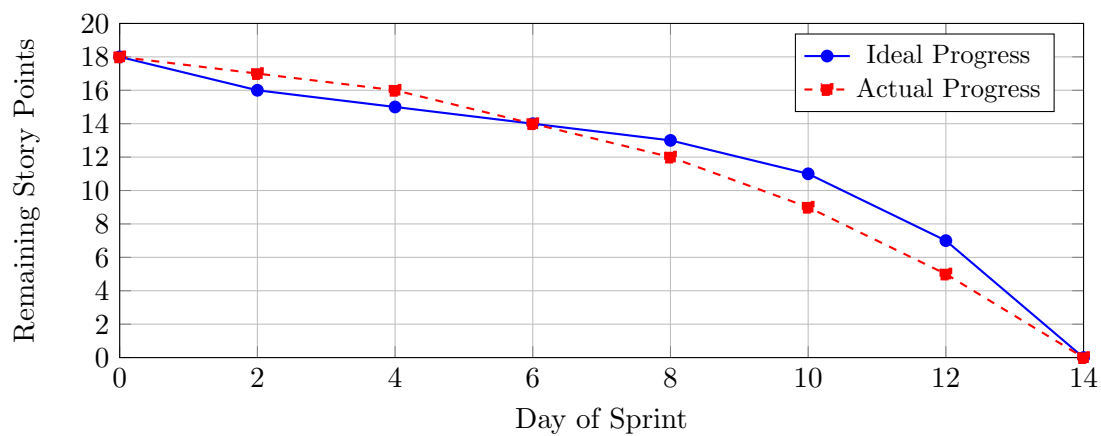


📊 Story Point Completion


Total: 18 Story Points

By Priority

Team Contribution

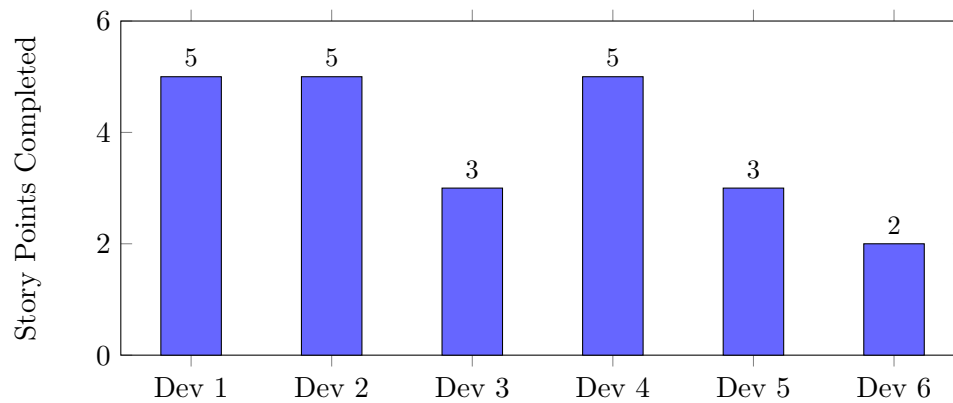


Sprint Timeline & Key Events

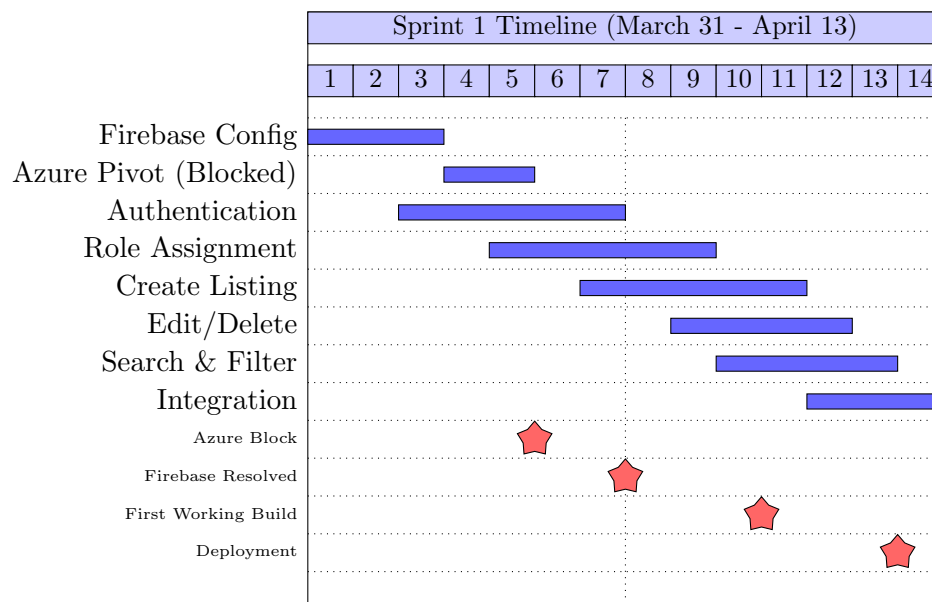

✓ User Stories Completed

Story	Developer	Status
Student registration & login (US1)	Dev 1, Dev 2	✓Complete
Role assignment (US2)	Dev 3	✓Complete
Create an item listing (US3)	Dev 4	✓Complete
Edit or remove a listing (US4)	Dev 5	✓Complete
Mark listing type & search/filter (US5)	Dev 6	✓Complete

⚠ Challenges & Resolutions

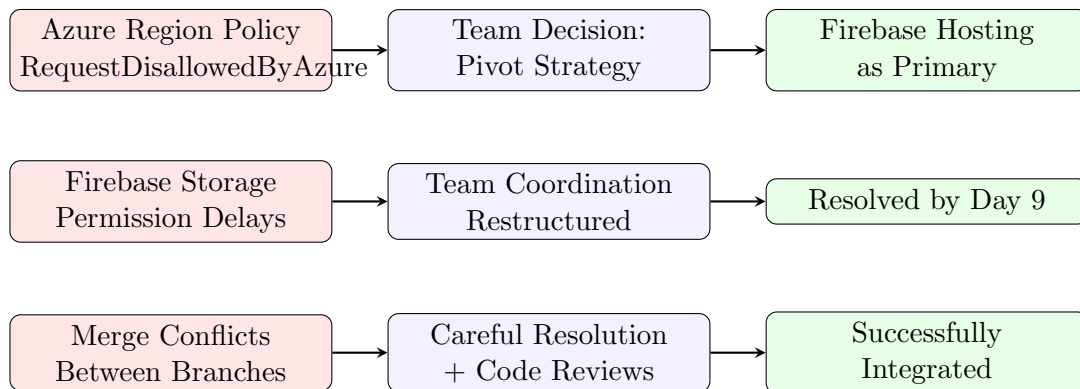

☁ Infrastructure Architecture

(Secondary/Fallback);
 [arrow] (github) – (actions); [arrow] (actions) – (firebasehost); [arrow] (firebasehost) – (firebaseauth); [arrow] (firebasehost) – (firestore); [arrow] (firebasehost) – (storage);
 [arrow,dashed] (actions) – (azure);

💻 What Was Demonstrated

- ✔ Google OAuth login via Firebase
- ✔ Role-based dashboard routing
- ✔ Create listings with photos
- ✔ Edit and delete own listings
- ✔ Listings with category, condition, price
- ✔ Browse page with search & filter
- ✔ App deployed and accessible online
- ✔ Vitest unit tests with coverage

⌚ What Was Not Completed / Blocked

- ❌ **Firebase Auth not fully integrated** — edit/delete uses sessionStorage temporarily pending Auth completion
- ⚠ **Firestore security rules** — pending role schema finalisation from Dev 3
- ⚠ **Firebase Storage permissions** — required team coordination and caused delays early in the sprint

Team Reflections

Developer	Key Reflection
Dev 1 (Kgethego)	Managed infrastructure pivot from Azure to Firebase, maintained project documentation and sprint governance
Dev 2 (Nontokozo)	Authentication implemented successfully, integration with other features in progress
Dev 3 (Athalia)	Successfully implemented Firebase Storage and role assignment despite initial blockers
Dev 4 (Victor)	Successfully implemented listing creation using React in a short period
Dev 5 (Tebogo)	Built edit/delete feature with TDD approach, resolved merge conflicts
Dev 6 (Mmaphefo)	Implemented dynamic search and filtering — will improve testing strategy in Sprint 2

Key Metrics

Metric	Value
Story Points Planned	18
Story Points Completed	18 (100%)
User Stories Completed	5/5 (100%)
Days in Sprint	14
Team Members	6
Infrastructure Pivots	1 (Azure → Firebase)
Merge Conflicts Resolved	4
