

CampusMarket

Agile Sprint Report

Sprint Backlogs • Burndown Charts • Statistics • Project Analysis

A web-based peer-to-peer trading platform for university students

4 Sprints | 8 Weeks | 38 Items | 147 Story Points | All Done ✓

Project Brief Summary

CampusMarket is a web-based peer-to-peer trading platform built exclusively for university students. The platform enables students to list, discover and safely exchange or trade new and used items within their campus community. A secure trade management facility handles drop-off and collection, and all payments are made online, with cash shortfalls supplemented by cash payment through the same payment platform.

Core Objectives

- Item listing and browsing system
- Secure trade facility management (drop-off and collection)
- Built-in messaging system between buyers and sellers
- Online payments with cash shortfall supplement
- Rating and trust system for campus community safety
- Analytics dashboards with CSV/PDF export capability

Detailed Requirements

Requirement	Description	Extra Info / Limitations
User Verification	A third-party identity provider should be used. 3 roles: Student, Trade Facility Staff, Admin.	Firebase Authentication implemented for all role types.
Listing Management	Students can add, edit and remove item listings with photos, descriptions, categories, condition ratings and asking prices.	Listings should indicate if the item is for sale, trade, or both.
Buyer Experience	Buyers can search by category, filter by price & condition, initiate a purchase or trade offer, and view seller ratings.	All payments made online via the platform.
Trade Facility Management	Staff can manage drop-off and collection bookings, confirm item receipt and release, and update transaction status.	Admins can configure facility operating hours and slot capacity.
In-App Messaging	Buyers and sellers can communicate through a built-in chat to negotiate and arrange transaction details before committing.	Must happen before a trade facility booking is committed.
Payments	Integrated with a 3rd-party payment gateway. Students can pay full or partial amounts, with cash shortfall tracked and settled.	Staff must confirm all cash components are settled before releasing items.
Rating & Trust System	Both parties can leave ratings and reviews after a completed transaction. Admins can flag or remove abusive content.	Contributes to seller credibility on the platform.

SA Data Integration	Price suggestions informed by publicly available South African consumer price data relevant to the item category.	Must document the data source and justify its suitability for the project backlog.
Analytics	At least 3 dashboard reports: popular categories & completed transactions over time, trade facility utilization, flagged/moderated content summary.	Reports must be exportable as CSV or PDF. Bonus: ML integration for price suggestions.


Project Overview & Statistics

CampusMarket was developed over an 8-week timeline across 4 Scrum sprints, followed by a dedicated finalisation week for QA, deployment and handover. All 38 backlog items were delivered, covering every requirement in the project brief.

Sprint Summary Table


Sprint	Duration	# Items	Story Points	Velocity (pts/day)	Sprint Goal	Status
Sprint 1	2 Weeks	16	50	3.6	Foundation	Done ✓
Sprint 2	1 Week	6	26	3.7	Core Features	Done ✓
Sprint 3	3 Weeks	12	41	2.0	Payments & Analytics	Done ✓
Sprint 4	1 Week	4	29	4.1	Safeguards	Done ✓
TOTAL	8 Weeks	38	146	3.0	Full MVP	Done ✓

Project Timeline

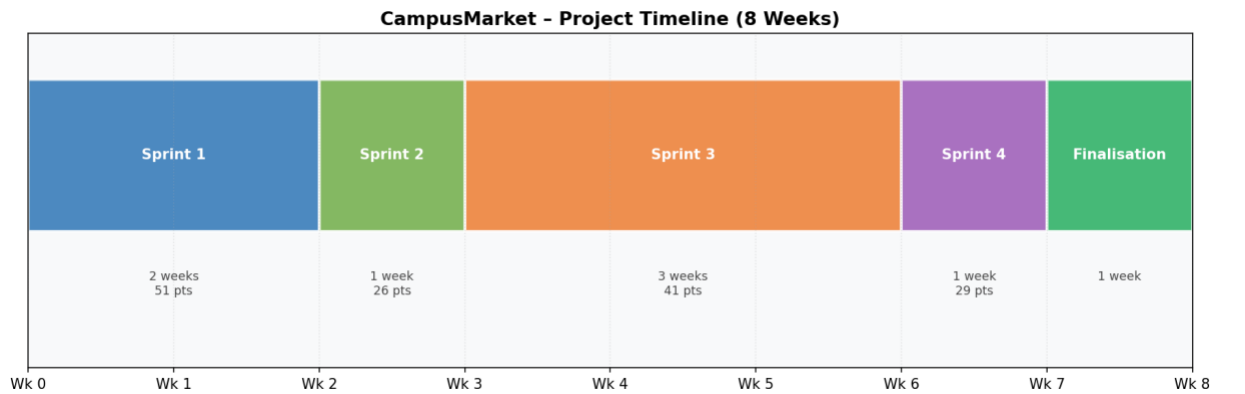

Sprint Comparison Charts

CampusMarket Project - Sprint Comparison

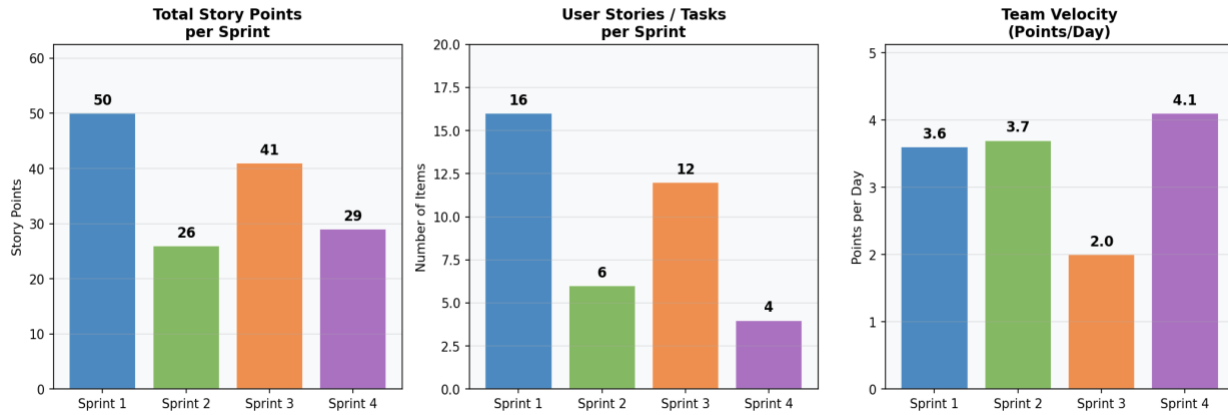

Project Burn-Up Chart

CampusMarket - Project Burn-Up Chart
(8-Week Timeline: 4 Sprints + Finalisation)



Sprint 1 – 2 Weeks

Sprint Goal: Project foundation: environment setup, authentication, role management, item listings, wireframes, architecture, CI/CD pipeline and documentation.


Duration: 2 Weeks (14 days) | Story Points: 50 | Items: 16 | Velocity: 3.6 pts/day

Sprint 1 Backlog

User Story / Task	Story Points	Status	Priority
Project setup & Firebase config	3	Done ✓	Low
US1: Implement User Authentication (Firebase)	5	Done ✓	Medium
US2: Role assignment – Role-based access control	3	Done ✓	Low
US3: Create an item listing	5	Done ✓	Medium
US4: Edit or remove a listing	2	Done ✓	Low
US5: Listing type	2	Done ✓	Low
Design wireframes for core screens	3	Done ✓	Low
System Architecture	3	Done ✓	Low
Create ERD (Entity Relationship Diagrams)	3	Done ✓	Low
Create use case diagrams	3	Done ✓	Low
Create Test plan documentation	2	Done ✓	Low
Set up CI/CD pipeline using GitHub Actions	5	Done ✓	Medium
Record daily scrum meeting minutes	1	Done ✓	Low
Design admin dashboard wireframes	5	Done ✓	Medium
Create high-fidelity mockup	3	Done ✓	Low
Create project overview documentation	2	Done ✓	Low
SPRINT TOTAL	50		


Sprint 1 – Story Points Breakdown

Sprint 1 - Story Points per Item

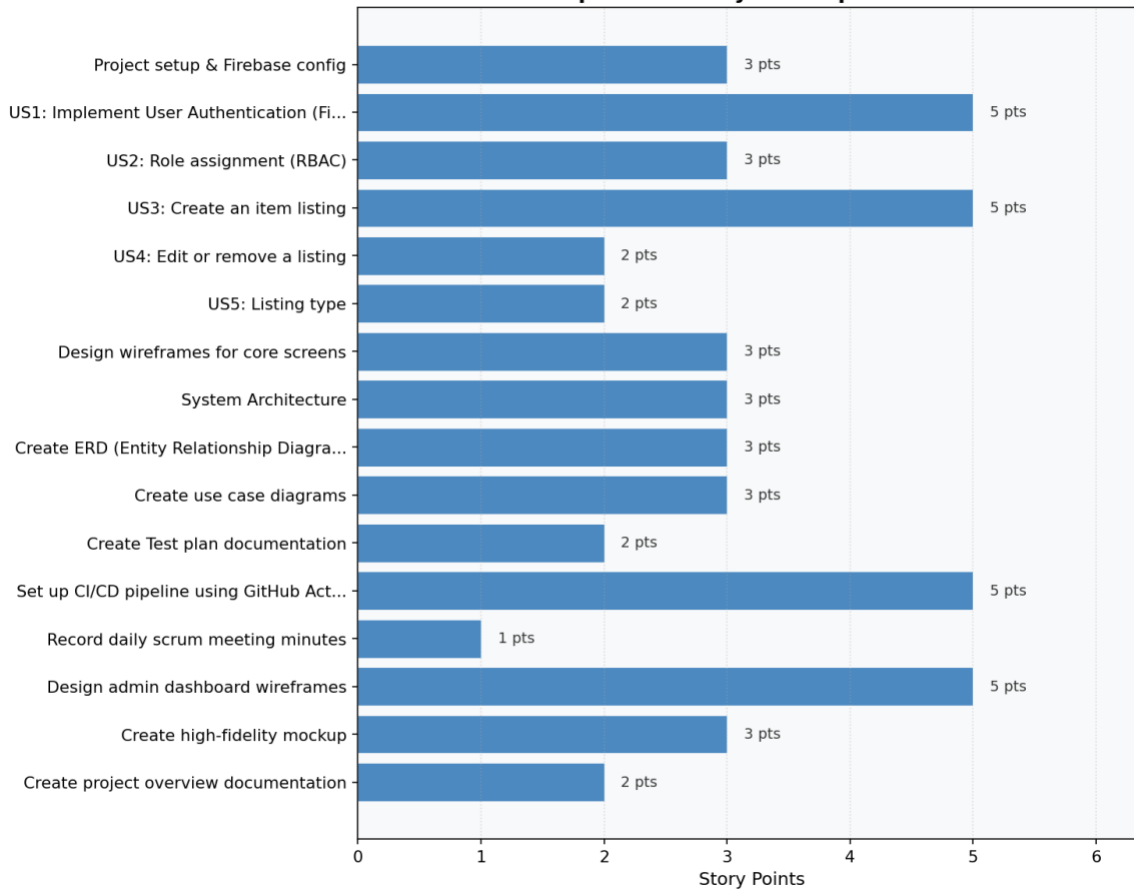

Sprint 1 – Burndown Chart

Sprint 1 - Burndown Chart
(Total: 50 story points, 14 days)

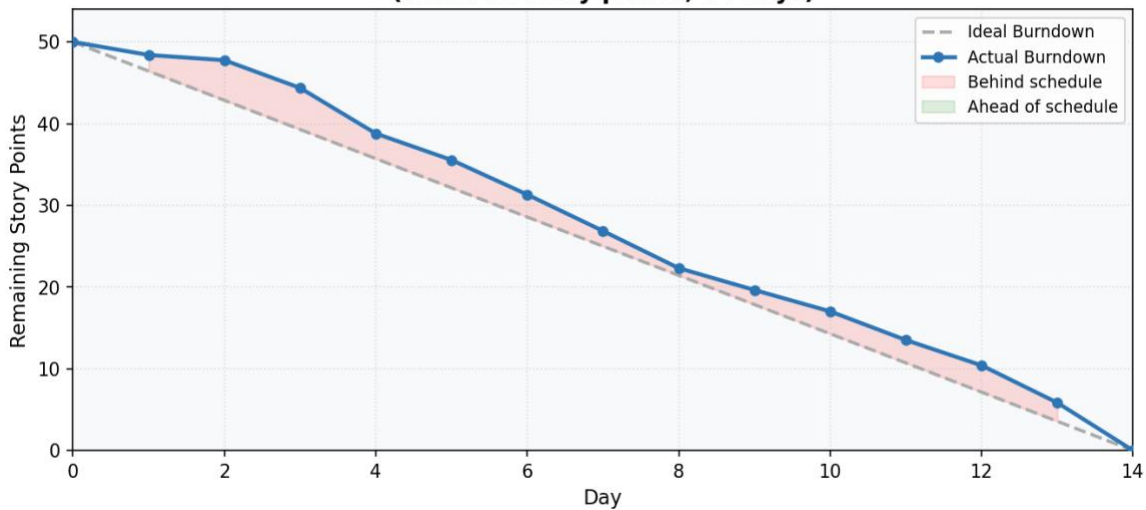

Sprint 1 – Sprint Statistics

Metric	Value	Notes
Sprint Duration	2 Weeks (14 days)	Calendar duration
Total Story Points	50	All items completed
Number of Items	16	User stories & tasks
Team Velocity	3.6 pts/day	Story points per day
Highest Effort Item	US1: Implement User Authentication (Fire...	5 pts
Completion Rate	100%	All items Done ✓

Sprint 2 – 1 Week


Sprint Goal: Core marketplace functionality: drop-off booking, buyer/seller interaction, ratings, dashboards and purchase initiation.

Duration: 1 Week (7 days) | Story Points: 26 | Items: 6 | Velocity: 3.7 pts/day

Sprint 2 Backlog


User Story / Task	Story Points	Status	Priority
US10: Book Drop-Off Slot	3	Done ✓	Low
US7: View Seller Rating	2	Done ✓	Low
US9: Buyer-Seller Chat (In-App Messaging)	5	Done ✓	Medium
US16: Leave Rating and Review	3	Done ✓	Low
US23: Build Role-Based Dashboards and Profile Views	8	Done ✓	High
US8: Initiate Purchase or Trade Offer	5	Done ✓	Medium
SPRINT TOTAL	26		

Sprint 2 – Story Points Breakdown

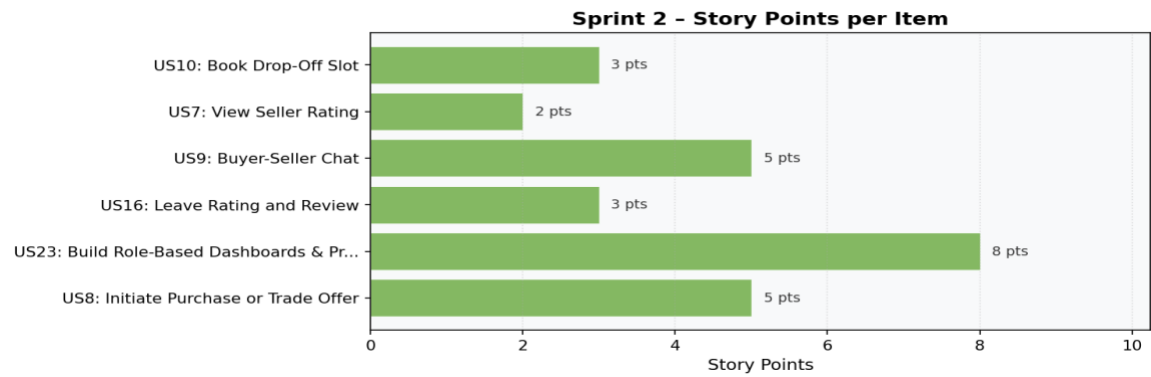

Sprint 2 – Burndown Chart

Sprint 2 - Burndown Chart
(Total: 26 story points, 7 days)

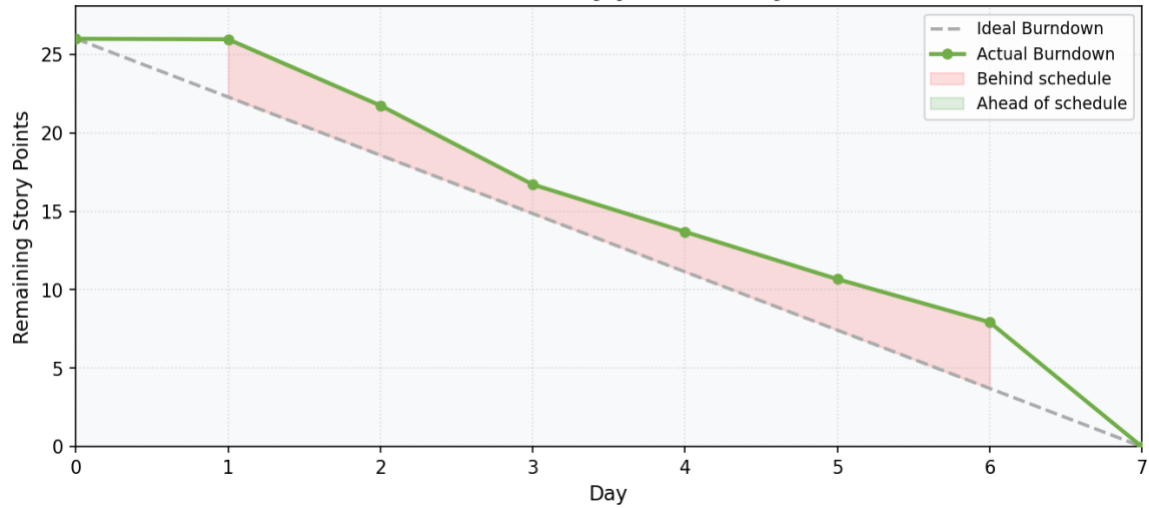

Sprint 2 – Sprint Statistics

Metric	Value	Notes
Sprint Duration	1 Week (7 days)	Calendar duration
Total Story Points	26	All items completed
Number of Items	6	User stories & tasks
Team Velocity	3.7 pts/day	Story points per day
Highest Effort Item	US23: Build Role-Based Dashboards and Pr...	8 pts
Completion Rate	100%	All items Done ✓

Sprint 3 – 3 Weeks

Sprint Goal: Payments, facility management, content moderation, SA data integration, analytics dashboards and reporting exports.


Duration: 3 Weeks (21 days) | Story Points: 41 | Items: 12 | Velocity: 2.0 pts/day

Sprint 3 Backlog

User Story / Task	Story Points	Status	Priority
US20: Trade Facility Utilization Report	2	Done ✓	Low
US12: Configure Facility Hours and Capacity	2	Done ✓	Low
US11: Staff Confirm Item Receipt and Release	3	Done ✓	Low
US13: Online Payment (3rd-party gateway)	8	Done ✓	High
US14: Partial Payment with Cash Shortfall	3	Done ✓	Low
US15: Staff Confirm Cash Shortfall Settled	2	Done ✓	Low
US17: Moderate Abusive Content	2	Done ✓	Low
US18: Price Suggestions for Listings (SA Data Integration)	8	Done ✓	High
US19: Popular Categories Report	3	Done ✓	Low
US21: Moderated Content Summary Report	2	Done ✓	Low
US22: Export Reports as CSV or PDF	3	Done ✓	Low
US24: Banner Interaction – Bottom Fixed Banner (Ads)	3	Done ✓	Low
SPRINT TOTAL	41		


Sprint 3 – Story Points Breakdown

Sprint 3 - Story Points per Item

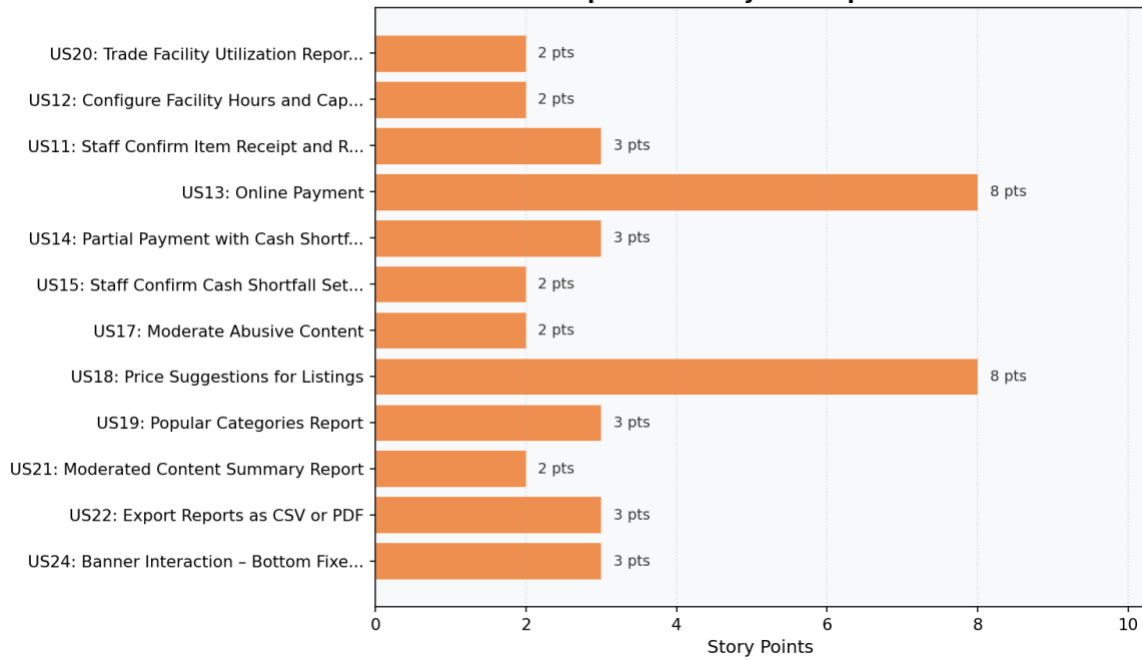

Sprint 3 – Burndown Chart

Sprint 3 - Burndown Chart
(Total: 41 story points, 21 days)

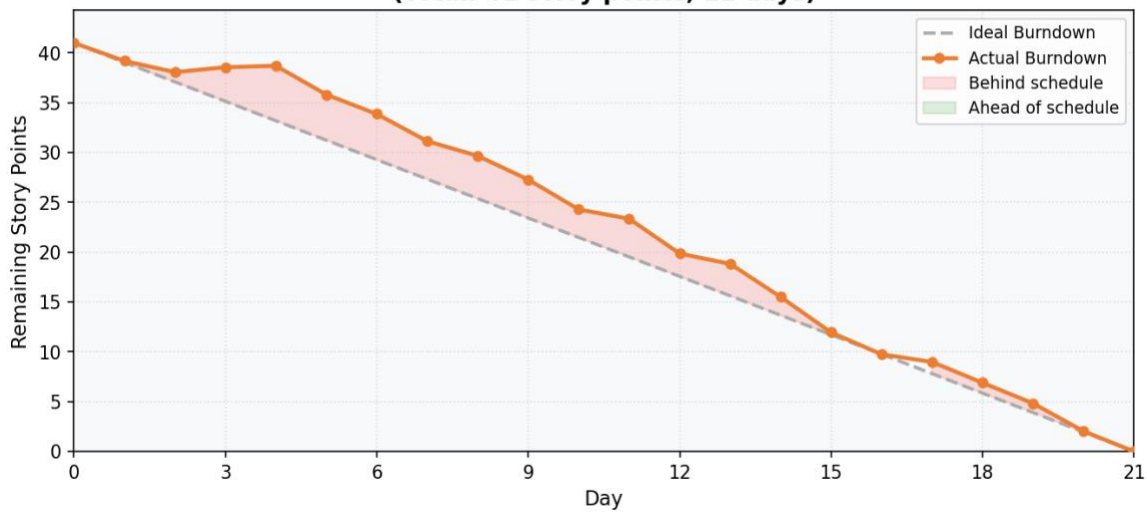

Sprint 3 – Sprint Statistics

Metric	Value	Notes
Sprint Duration	3 Weeks (21 days)	Calendar duration
Total Story Points	41	All items completed
Number of Items	12	User stories & tasks

Team Velocity	2.0 pts/day	Story points per day
Highest Effort Item	US13: Online Payment (3rd-party gateway)	8 pts
Completion Rate	100%	All items Done ✓

Sprint 4 – 1 Week


Sprint Goal: Transaction safeguards: cancellation flows, trade-instead-of-payment feature, date restrictions and automated overdue notifications.

Duration: 1 Week (7 days) | Story Points: 29 | Items: 4 | Velocity: 4.1 pts/day

Sprint 4 Backlog


User Story / Task	Story Points	Status	Priority
US26: Cancel Initiation of Purchase	5	Done ✓	Medium
US27: Restrict drop-off dates – max 7 days after buyer paid	3	Done ✓	Low
US28: Allow students to trade items instead of direct payments	13	Done ✓	High
US29: Notify seller about overdue drop-off & auto-cancel after grace period	8	Done ✓	High
SPRINT TOTAL	29		

Sprint 4 – Story Points Breakdown

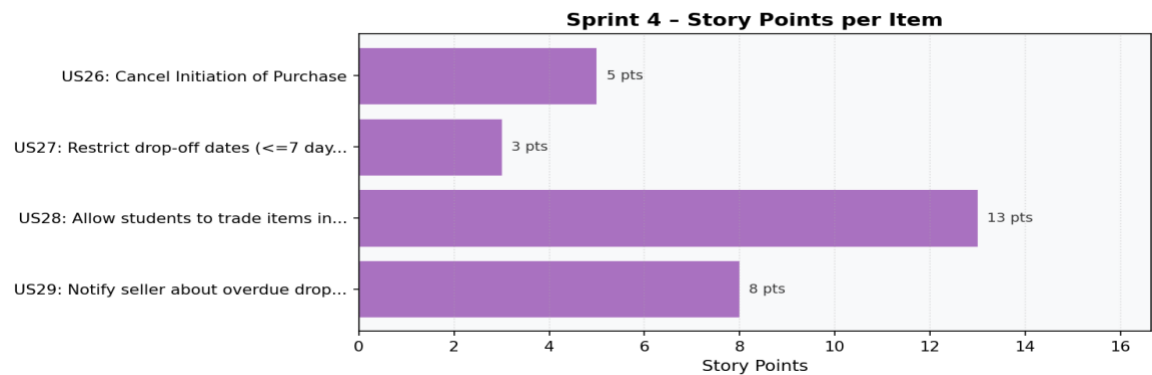

Sprint 4 – Burndown Chart

Sprint 4 - Burndown Chart
(Total: 29 story points, 7 days)

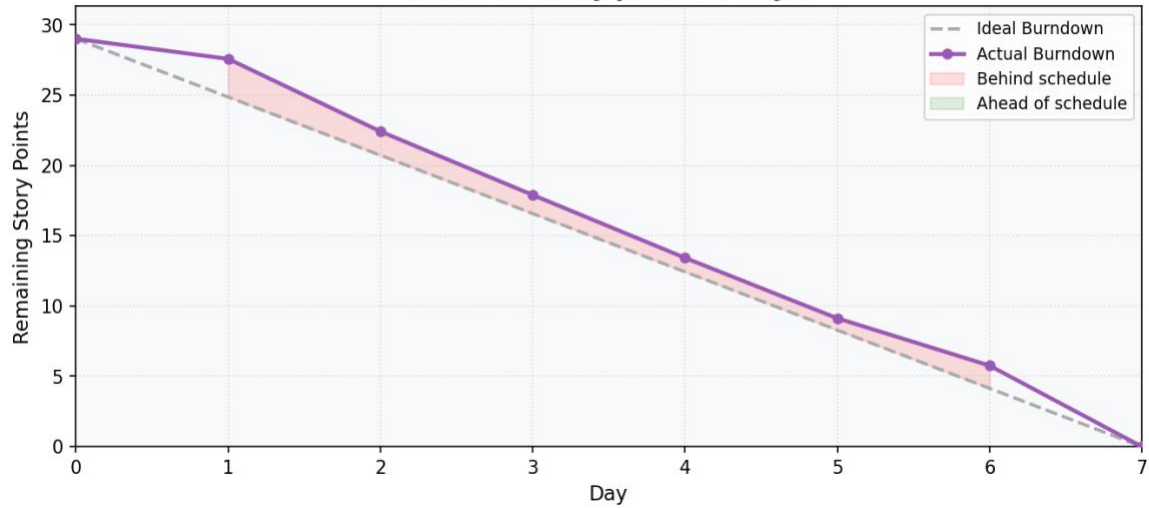

Sprint 4 – Sprint Statistics

Metric	Value	Notes
Sprint Duration	1 Week (7 days)	Calendar duration
Total Story Points	29	All items completed
Number of Items	4	User stories & tasks
Team Velocity	4.1 pts/day	Story points per day
Highest Effort Item	US28: Allow students to trade items inst...	13 pts
Completion Rate	100%	All items Done ✓

Finalisation Week – Week 8

The final week of the project was dedicated to quality assurance, documentation completion, deployment preparation and project handover. No new features were developed during this phase.

Activity	Description
Final QA & Testing	End-to-end testing of all user flows including payments, trade facility booking, chat and admin dashboards.
Documentation Review	Final review of all sprint documentation, test plans, ERDs, architecture diagrams and user stories.
Deployment Preparation	CI/CD pipeline final checks, environment configuration, production deployment readiness.
Sprint Retrospective	Full project retrospective: what went well, areas for improvement, lessons learned and action items.
Project Handover	Demo preparation, final report submission and project artefact handover to reviewers/assessors.
